

Traceability Map

Planning Phase

Cloud Migration Project

Document ID: CMP-PLA-00


srk

Planning — Traceability & Dependency Map

Cloud Migration Project

Document ID: CMP-PLAN-00 **Version:** 1.0 **Date:** 2026-08-26 **Upstream Input:** Initiation (CMP-INIT-07 Project Charter, CMP-INIT-06 RAID, CMP-INIT-04 Stakeholder Register, CMP-INIT-05 RACI, CMP-INIT-03 Scope)

Dependency Tree

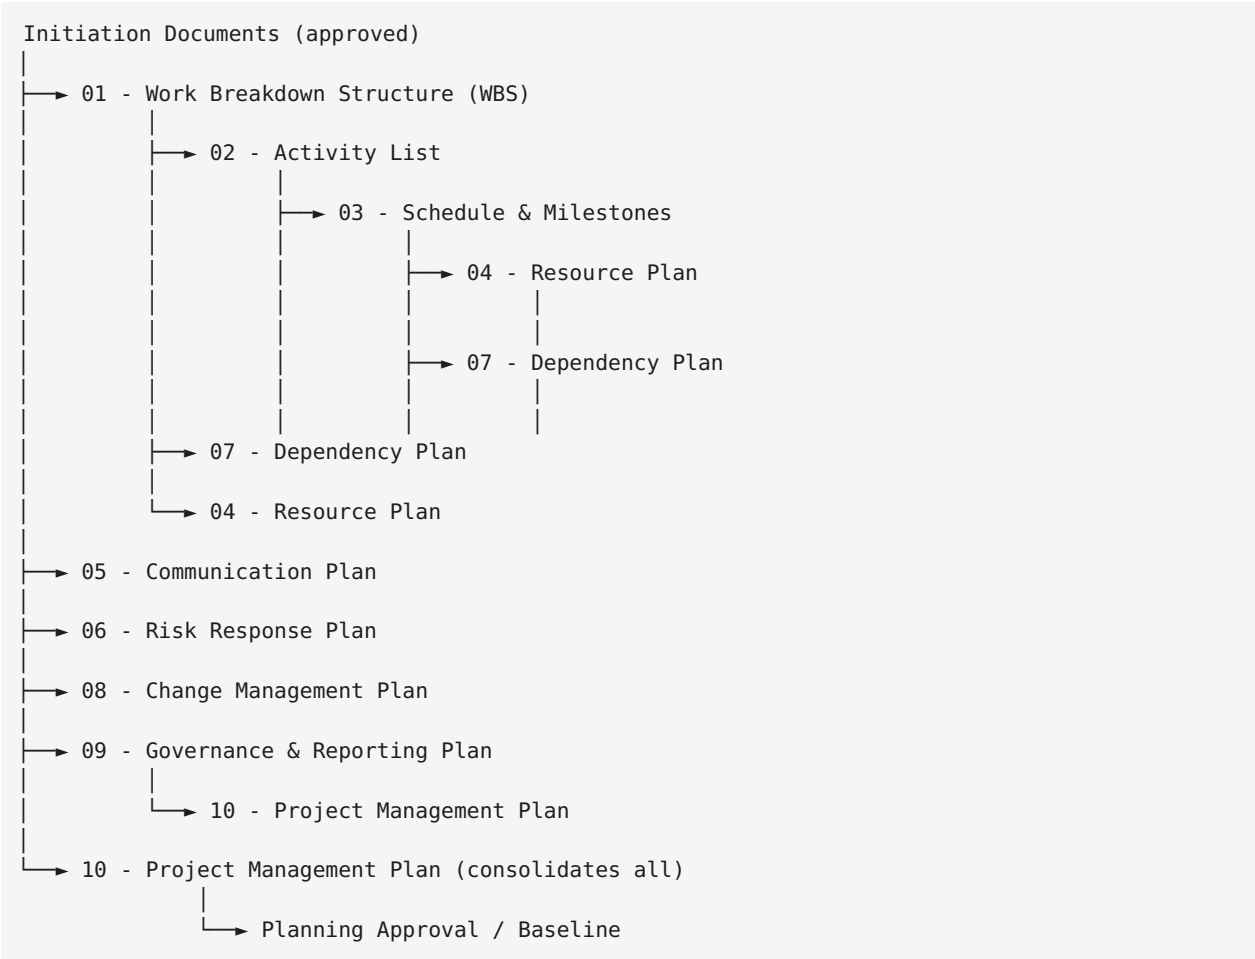

Traceability Table

Doc	Document Name	Depends On (Planning)	Depends On (Initiation)	Provides Input To
01	WBS	None	Charter, Scope, Deliverables	02, 03, 04, 07
02	Activity List	01	WBS	03, 04, 07
03	Schedule & Milestones	01, 02	Charter, Dependencies	04, 07, 10
04	Resource Plan	01, 02, 03	RACI, Stakeholder Register	10
05	Communication Plan	None	Stakeholder Register, RACI, Schedule, Governance	09, 10
06	Risk Response Plan	None	Initial RAID	10
07	Dependency Plan	01, 02, 03	RAID, Stakeholder Register	10
08	Change Management Plan	None	Charter, Scope, Stakeholder Register, Governance	10
09	Governance & Reporting Plan	05	Stakeholder Register, RACI, Charter	10

Doc	Document Name	Depends On (Planning)	Depends On (Initiation)	Provides Input To
10	Project Management Plan	01-09	All Initiation docs	Planning Approval

Dependency Matrix

	01	02	03	04	05	06	07	08	09	10
01	—									
02	●	—								
03	●	●	—							
04	●	●	●	—						
05					—					
06						—				
07	●	●	●				—			
08								—		
09					●				—	
10	●	●	●	●	●	●	●	●	●	—

● = Row depends on Column

Initiation → Planning Handoff

Initiation Document	Planning Document(s) That Use It
01 - Problem Statement	(indirectly via Charter)
02 - Business Objectives	(indirectly via Charter)
03 - Project Scope	01-WBS, 08-Change Management
04 - Stakeholder Register	04-Resource Plan, 05-Communication, 07-Dependency, 08-Change, 09-Governance
05 - RACI Matrix	04-Resource Plan, 05-Communication, 09-Governance
06 - Initial RAID	06-Risk Response, 07-Dependency
07 - Project Charter	01-WBS, 03-Schedule, 08-Change, 09-Governance
08 - Approval Authorization	Authorizes Planning phase

Validation Rule

Planning documents cannot be baselined until: 1. All Initiation documents are approved 2. All Planning documents they depend on are completed 3. The Project Management Plan (10) consolidates and validates all planning artifacts
