

Traceability Map

Monitoring Phase

Cloud Migration Project

Document ID: CMP-MON-00

srk

Monitoring & Controlling — Traceability & Dependency Map

Cloud Migration Project

Document ID: CMP-MON-00 **Version:** 1.0 **Date:** 2026-08-26 **Upstream Input:** Planning Baseline (CMP-PLAN-10), Execution Documents (CMP-EXEC-01 through CMP-EXEC-05), Jira Operational Data

Dependency Tree




Traceability Table

Doc	Document Name	Depends On (Monitoring)	Depends On (Execution/Planning)	Provides Input To
01	Project Baseline	None	Planning Baseline (CMP-PLAN-10)	02, 03, 04, 05, 06
02	Performance Dashboard	01, 03, 04, 05, 06	Execution Tracker, Jira	07, 09
03	Schedule Monitoring	01	Execution Tracker, Jira	02, 07

Doc	Document Name	Depends On (Monitoring)	Depends On (Execution/Planning)	Provides Input To
04	Scope Monitoring	01	Change Log, WBS	02
05	RAID Review	01	Risk Response Plan, Execution MoM	02, 07, 09
06	Milestone Monitoring	01	Schedule, Jira	02, 09
07	Weekly Monitoring Reports	02, 03, 05	Execution data	08, 09
08	Escalation Log	07	Weekly Reports	09
09	Steering Committee Updates	02, 05, 06, 08	All monitoring data	Closure

Execution → Monitoring Continuous Loop

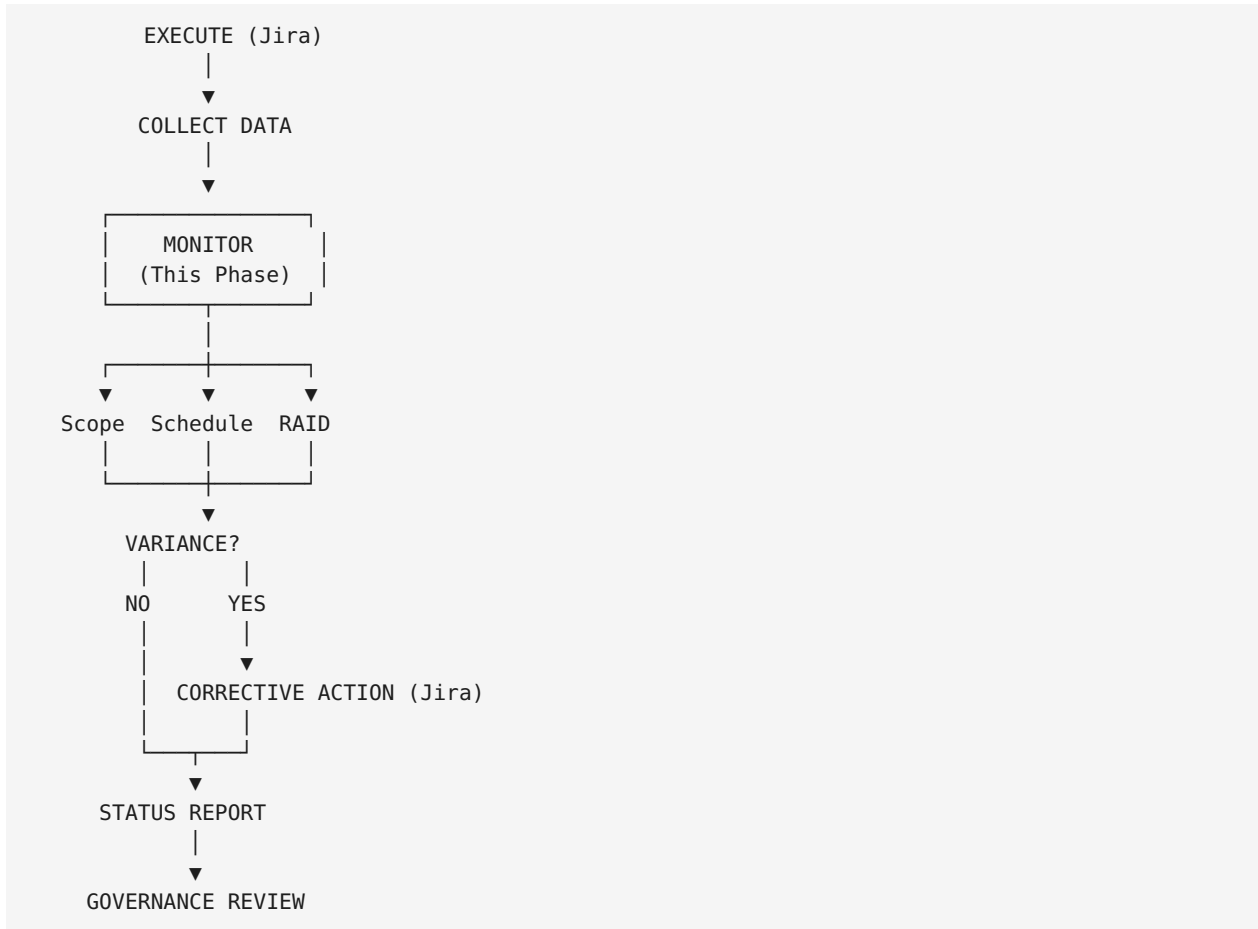

Corrective Action Flow

Step	Activity	Tool	Output
1	Variance detected	Monitoring documents	Variance identified
2	AI analysis	AI prompt	Root cause + options
3	PM decision	PM judgment	Corrective action approved
4	Jira task created	Jira	Actionable work item
5	Action executed	Jira	Work completed
6	Outcome verified	Monitoring documents	Variance resolved or not
7	Reported	Weekly/Steering reports	Stakeholders informed
